

Seta Future — Phase-1 Kickoff Signoff

Field	Value
Document	Project signoff for kickoff
For	CEO · CTO · PMO
Author	Project Management Office
Kickoff (actual)	2026-04-23 (S1–S2 complete on provisional approval)
First demo	2026-05-20 (interim · end of S4)
MVP demonstration	2026-05-31 (staging only · 6-week window)

1. Why this matters

Ship Future Phase-1 MVP — **Planner + Agents** + platform core — on staging by **2026-05-31** with 6.0 FTE in 6 weeks.

Problem today	Outcome at MVP
Project data is siloed — each SETA project runs its own tools, no shared truth	Single source of truth across modules — people, tasks, plans, evidence, audit all live in one tenant-scoped platform
No company-wide task management — management has no cross-team visibility, no roll-up	Unified task management — plans/tasks/evidence + role-scoped views (IC throughput · team-lead balance · org-leader cross-team risk)
M365 Planner has no evidence, personal hubs, audit history	Evidence-backed completion · 4 personal hubs · audit · bidirectional M365 sync
No governed AI surface for staff	AI-as-a-Service for every employee — KB Q&A with citations · role-scoped Planner analysis · natural-language task control via approval inbox
AI-leveraged delivery velocity is unmeasured	S3 retro re-baselines burn (~45 SP/eng/sprint forecast) — sizing artefact for the rest of the build
Every later module would re-solve identity, tenancy, audit	Platform core (kernel/RLS · identity · approval inbox · agent runtime · M365 connector) built once

2. Scope — What Ships by 2026-05-31

Two modules in scope: **Agents** (§9) and **Planner** (§10). Out of scope is the inverse — module-specific cuts in §9.3 and §10.2; programme-wide cuts cover other domain modules, manager dashboards, multi-language UI, native mobile, multi-region, Slack/Teams/Outlook, external tenants.

2.1 Acceptance criteria — demo on 2026-05-31

Live, end-to-end run on real SETA data on staging (post-MVP gates: §2.2).

1. SSO + magic-link login (Entra).
2. **Plan & tasks** — CRUD with assignees / dates / labels / checklists / attachments; Board · Grid · Charts · Schedule views; My Day + My Tasks hubs.
3. **Evidence flow** — complete-with-evidence → approval inbox → M365 sync; conflicts logged with field-level diff.
4. **AI — KB Q&A** with citations, ≥80% rubric accuracy.
5. **AI — Planner analysis** — natural-language queries, role-scoped views, k-anonymity, cites tasks.
6. **AI — inline copilot** + daily digest (next business day).
7. **AI — Planner control** — natural-language intent → write → inbox → approval → M365.
8. **Multi-tenant probe** — leak canary green.
9. **Failure modes** — cost-ceiling tripwire, KB-miss refusal, idempotent sync retries.
10. **Admin** — sync-health · conflict log · cost ledger · audit query.


Perf gates: Board $p95 \leq 400\text{ ms}$ · My Tasks $p95 \leq 1.0\text{ s}$ · agent $p95 \leq 8\text{ s}$ · zero leak. **Quality:** ≥70% unit coverage (CI-blocking) + Playwright E2E on the four golden flows (login · KB Q&A · evidence→approval→sync · tenant isolation). **Security:** secrets in AWS Secrets Manager · RLS coverage green · dep/container scans clean · M365 tokens encrypted+rotating · staff comms sent.

2.2 What 2026-05-31 is — and is not

✔ It is	✖ It is not
MVP demo on real SETA data, staging only	GA · production · external pilot
Internal-use ready (SETA staff)	External-tenant ready (GDPR erasure)
PMO performance anchor for the programme	An all-modules platform

Post-MVP gates: production cutover · agent writes (Agents SAD §9.3) · Planner launch 2026-06-08 (Planner SAD §9.1).

3. Timeline — Six One-Week Sprints

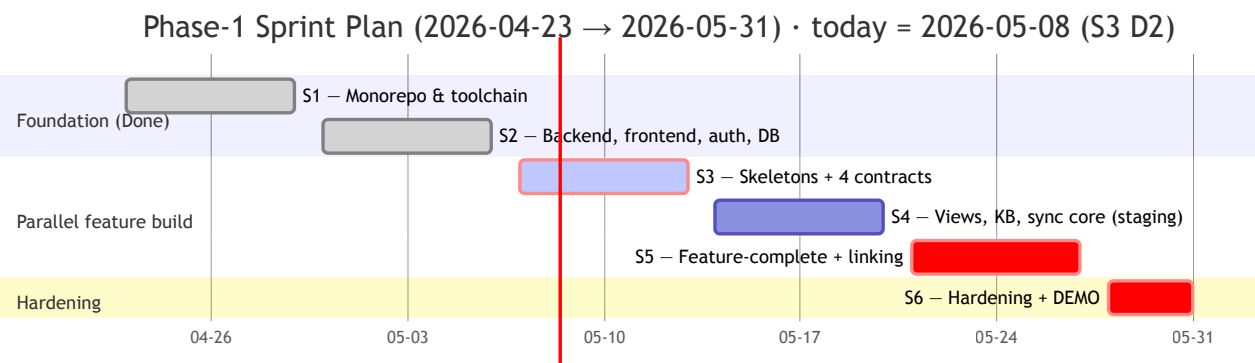

Sprint	Window	Goal	Gate
S1	04-23 → 04-29	Monorepo + toolchain — Done	—
S2	04-30 → 05-06	Backend / frontend / auth / DB skeletons + SSO — Done	—
S3	05-07 → 05-13	Staging deployable · Planner CRUD · Agents chat skeleton · 4 contracts D1	Velocity re-baseline retro
S4	05-14 → 05-20	Planner views + hubs + sync · Agents KB + Q&A + write mode · staging hardened	First demo — 2026-05-20
S5	05-21 → 05-27	Feature-complete + linking · freeze at S5 close	Go / no-go for S6
S6	05-28 → 05-31	Hardening only — bugs, performance, accessibility, security, demo prep, traceability	MVP demo — 2026-05-31

3.1 Load-bearing date not on the gantt

S3 D2 (05-08) — M365 sandbox + Entra consent + Graph scopes (SETA IT); KB ingestion pipeline complete. Slips here cascade through S3 retro, first demo, and freeze.

3.2 Phase-1.5 cut order (pre-agreed, applies at S3 retro)

Apply in order until scope fits velocity: (1) scheduled digests · (2) bidirectional sync → one-way push · (3) Charts + Schedule views · (4) Personal Charts hub · (5) agent writes (already gated in Agents SAD §9.3).

4. Team — 6.0 FTE for 6 weeks

Role	FTE	Status	Owns
Planner Module	1 fullstack	0.5 existing + 0.5 to hire	Plans/tasks/evidence → views/hubs → M365 sync → linking
Agents Module	1 AI + 1 fullstack	1 AI existing · 1 fullstack to hire	Chat → KB → writes via inbox → admin/governance → linking
Deployment	1 DevOps	Existing (needs IT support)	Staging · web-shell SSO + magic-link · dual-tenant probe
QA Engineer	1.0	To hire — onboard now	Manual / exploratory / regression / launch-gate
Business Analyst	0.5	Existing	Requirements · acceptance · traceability · doc work-stream
Scrum Master	0.5	To hire — onboard now	Cadence · retros · impediments · velocity
Total	6.0	To hire: 1.5 fullstack + 1 QA + 0.5 Scrum Master	

Enabling support: IT/DevOps provides AWS, DNS, certs, M365 sandbox + Entra consent, shared Terraform + IAM.

5. Budget — Cloud + AI Envelope

Line item	USD/month	Status
AWS — staging \$127 + prod \$349 (post-MVP)	~\$476 (GA)	Budgeted
Claude Code Max (developer tooling)	~\$220	Budgeted
OpenAI inference — 300 staff · ~10 turns/day · 4-axis caps	~\$880	Budgeted
Team payroll (6.0 FTE × 6 weeks)	(existing)	Already approved
Monthly envelope (cap)	~\$2,100	Approve

One-offs: M365 sandbox (zero); KB ingestion (~\$0.20). **Variance:** ≥2× ceiling 7-day → review; ≥3× → admin alert.

6. Risks That Bear on Scope or Timeline


Each row needs a CEO/CTO/PMO ruling before signoff. Full register in the board paper.

#	Risk	P/I	Mitigation
R1	~45 SP/eng/sprint velocity is forecast, not measured	M / H	S3 retro re-baselines from real burn; under → §3.2 cut order
R2	Hires (1.5 fullstack + 1 QA + 0.5 Scrum Master) late vs. 05-07	H / H	Onboard now; each week of fullstack slip ≈ one §3.2 cut
R3	Single-fullstack Planner — bus factor	M / H	PR reviewer named; >3-day absence → §3.2 cut #2
R4	Single-AI Agents — bus factor	M / H	Fullstack cross-trained S2; >3-day AI absence → drop Agents to KB Q&A + chat
R5	M365 Graph throttling untested at SETA scale	M / M	S4 backfill rehearsal; adaptive cadence + pre-flight limits
R6	S5 overload — feature-complete + linking same week	M / H	Mid-week freeze threshold; behind → cut Planner UI polish + Agents model-degradation

7. Asks to BOD — Sign by 2026-05-13 (S3 retro)

1. **Authorise** scope, timeline, team, and budget (§2, §3, §4, §5).
2. **Hires** — authorise 1.5 fullstack + 1 QA + 0.5 Scrum Master immediately (R2). Each week of fullstack slip ≈ one §3.2 cut.
3. **M365** — confirm sandbox + Entra consent + Graph scopes today, 2026-05-08. Slip → §3.2 cut #2 activates.
4. **Rule on §6 risks** — R2 (hires) and R5 (M365 throttling) are time-sensitive; the rest can be ruled at S3 retro.
5. **Acknowledge agile delivery.** Demo-affecting changes communicated to CEO/CTO/PMO within 24h; non-material refinements land in the sprint demo.

8. Architecture at a Glance

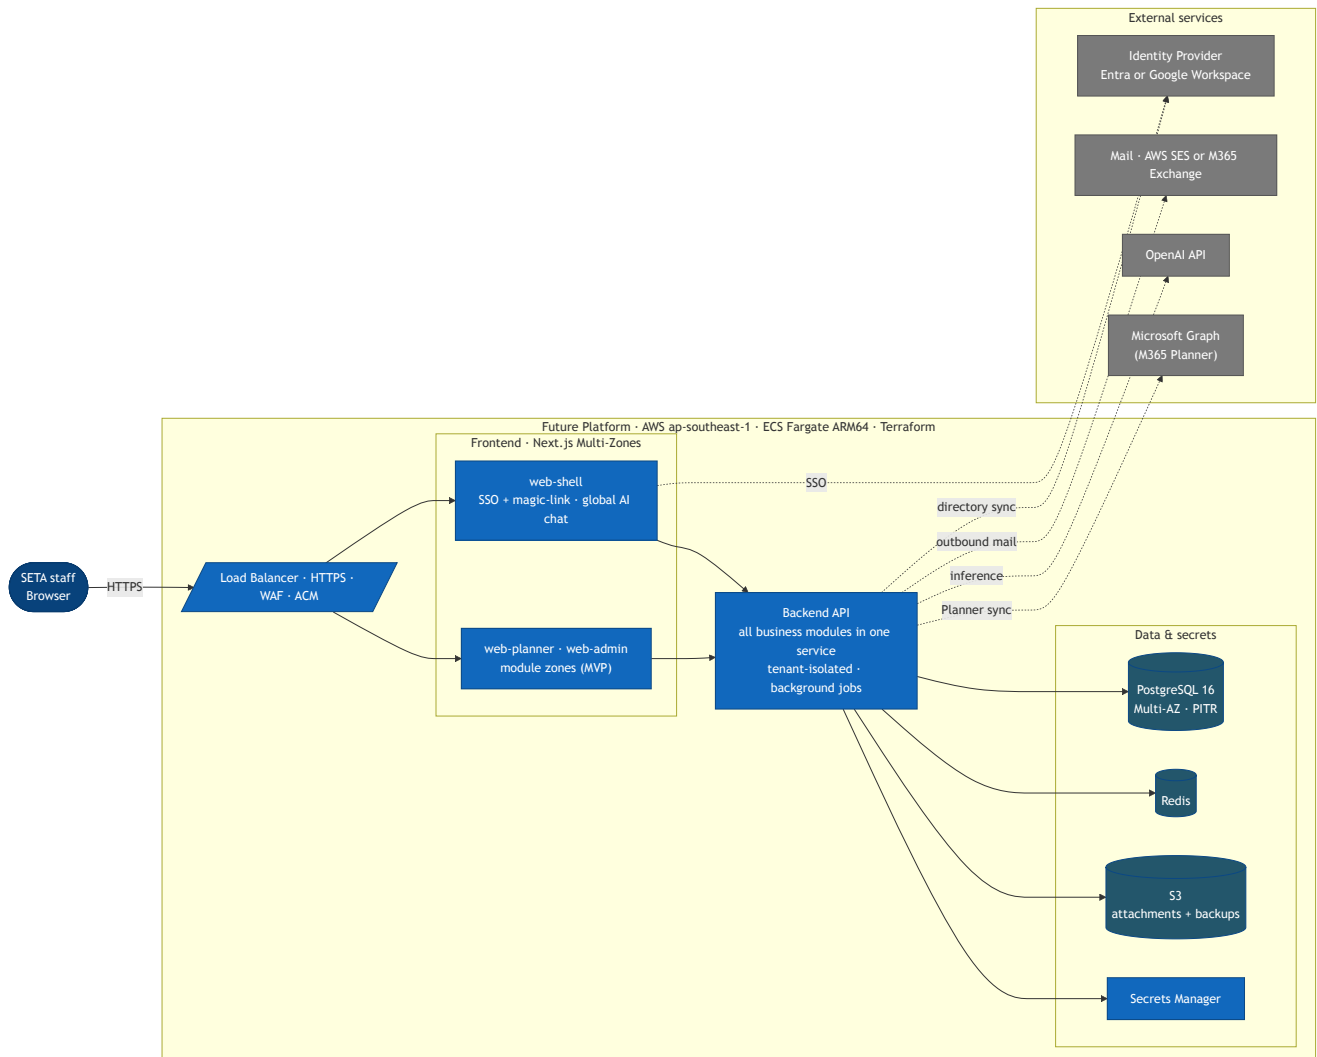


Invariants. Every table carries `tenant_id` with **RLS at the DB layer** · zones never query the DB directly (all data via tRPC) · **Terraform-only** infrastructure, no manual console changes · **ARM64 only** · secrets in AWS Secrets Manager.

9. Agents Module — Detailed Scope

9.1 Runtime architecture — one turn

Router plans → 1–2 sub-agents in parallel → Synthesizer. Every tool call goes through a non-skippable **Tool Gateway** (permission · audit · cost). Every LLM call lands in the replay-keyed **Prompt Store** — any past turn reconstructable by trace ID.

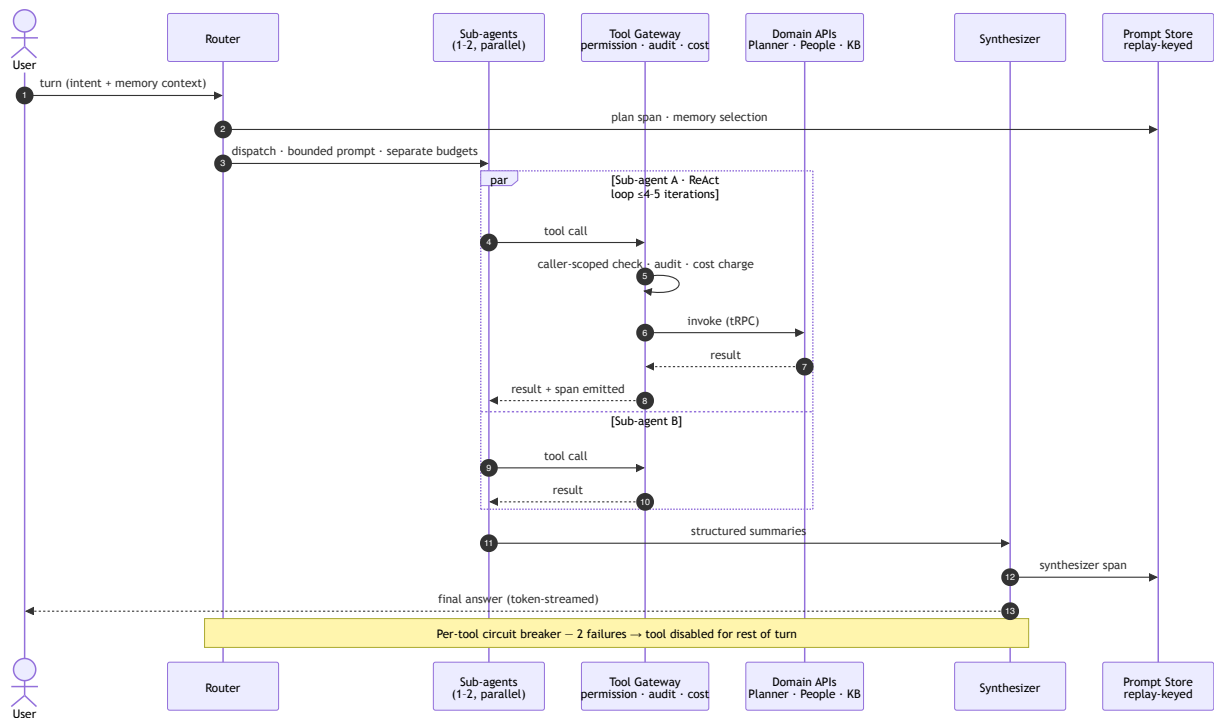

9.2 MVP capability buckets

Capability	What it does
Conversational surface	Global chat + inline Planner copilot; per-user threads with streaming
KB Q&A	Ingest Markdown / PDF / text; cited answers; admin upload · edit · deprecate · re-index
Planner query	Natural-language questions on tasks / workload / plan health; role-scoped views; k-anonymity on teams
Planner control (write)	Natural-language intent → structured write → approval inbox → executed on approval. Never silent, never autonomous
Scheduled digests	Opt-in morning brief · end-of-week status · stale-task nudges · at-risk alerts (read-only or inbox-draft)
Cost & governance	Four-axis USD ceilings (turn · user-day · tenant-day · delegation); admin controls model + visibility
Audit & replay	Caller-identity audit; deterministic replay from trace ID; plain-language refusal with reason

Router / sub-agents / Synthesizer / memory / ReAct / circuit-breaker internals: Agents SAD.

9.3 Agents-specific deferrals

- Cross-conversation memory (within-conversation only)
 - Autonomous writes (all writes go through inbox approval)
 - Event-triggered runs (cron only at MVP)
 - Meeting-transcript → plan conversion (Phase-1.5)
 - Image / OCR ingestion (text KB only)
 - Multi-provider routing (OpenAI only)
 - LLM-as-judge gating (deterministic scorers only)
-

10. Planner Module — Detailed Scope

Complements M365 Planner today and is positioned to replace it for non-M365 tenants. Future adds bidirectional sync, evidence-backed completion, personal hubs, and audit history M365 Planner doesn't provide. Architecture is provider-agnostic — Trello / Asana / Jira are post-MVP.

10.1 MVP capability buckets

Capability	What it does
Plans / buckets / tasks	Team + personal plans; ordered buckets; tasks (assignees, dates, labels, checklists, attachments, comments); soft-delete + audit
Four views	Board · Grid · Charts · Schedule (day/week/month). Shared filter+search. Not a Gantt
Four personal hubs	My Day · My Tasks · Personal Charts · Carry-Over (auto roll-forward)
Evidence	First-class records (file / link / note); unsubmitted → submitted → verified / rejected
M365 bidirectional sync	Tenant OAuth; adaptive pull + idempotent push; last-write-wins conflict log; dry-preview; revoke pauses within 1 cycle
Admin	Connect/disconnect · conflict log w/ field diff + force-resync · sync-health · attachment quotas

Field limits, FR-PL refs, Graph delta specifics: Planner SAD.

10.2 Planner-specific deferrals

- M365 Planner Premium tier (custom fields, sprints, M365 Copilot, rich-text, etc.)
- Gantt (Schedule = timeline-by-date, no dependencies / critical path)
- Real-time presence / cursors (async only)

- AI reminders & digests (live in Agents)
- Attachment processing (no OCR / virus scan / redaction)
- Per-field merge (last-write-wins fixed)
- Copy/template · Excel/CSV export · per-bucket colour (Phase-1.5)
- Push channels (pull-only)
- Asana / Trello / Jira (M365 only at MVP)

10.3 Hard external dependencies

Dependency	Owner	Deadline
M365 sandbox tenant + Entra admin consent + Graph scopes	SETA IT	2026-05-08
Secrets manager with online rotation for M365 credentials	Platform Security	S3
Identity directory sync (users, groups)	Identity / People	S3 D1 (05-07)

11. Sign-off

Role	Name	Signature	Date
CEO	Hung Vu		2026-05-08
CTO	Thu Mai		2026-05-08
PMO Lead	Hoang Nguyen		2026-05-08
